



ABN 41 004 669 658

G1 49 Melville Parade
South Perth WA 6151, Australia

PO Box 307
West Perth WA 6872, Australia

T 61 8 9474 2113
F 61 8 9367 9386

E info@randmining.com.au
W randmining.com.au

July 25, 2012

The Listing Manager
Australian Securities Exchange
Level 4
20 Bridge Street
SYDNEY NSW 2000

Quarterly Report for June 2012

Highlights

- During the quarter, 39,127 tonnes of EKJV ore were processed and 13,419 oz of gold and 4,926 oz of silver were credited to Rand and Tribune Bullion Accounts.
(Rand's share is 25%)
- At the end of the quarter
 - approximately 13,700 tonnes of Raleigh ore at an estimated grade of 17.9 g/t remain as a Bed Blend Stockpile on the ROM pad at the Raleigh Mine
(Rand's entitlement is 12.5%)
 - approximately 2,000 tonnes of Rubicon ore at an estimated grade of 14.5 g/t remain as a Bed Blend Stockpile on the ROM pad at the Rubicon Mine
(Rand's entitlement is 12.25%)
 - approximately 22,100 tonnes of Raleigh ore at an estimated grade of 14.8 g/t remains on the ROM pad at the Greenfields Plant
(Rand's share is 25%)
 - approximately 19,600 tonnes of Rubicon ore at an estimated grade of 9.3 g/t remains on the ROM pad at the Greenfields Plant
(Rand's share is 25%)
 - the difference of the Gold in Circuit at the start and end of Campaign 22 has been agreed and the amount, 3,679.888 oz, will be transferred to Rand and Tribune Bullion Accounts by the end of July.
(Rand's share is 25%)

GEOLOGY AND MINING

EAST KUNDANA JOINT VENTURE

Raleigh Underground Mine Production

Stope production from the 5949, 5932, 5915, 5898, 5881, 5864, 5847, 5830, 5812, 5795, 5778, 5761, 5744, 5722, 5705, 5688, 5671 and 5654 levels continued during the quarter.

Contained gold in stope development and stope ore mined during the quarter, estimated by grade control face chip sampling, is tabulated below:

RALEIGH UNDERGROUND GRADE CONTROL ESTIMATES			
Month	Tonnes	Grade	Ounces
	t	g/t	troy oz
April	18,752	16.97	10,234
May	14,485	17.57	8,180
June	20,904	17.23	11,583
June 12 Q	54,141	17.2	29,997
March 12 Q	63,933	14.5	29,850

Rand's Entitlements (12.5%)

June 12 Q	6,768	17.2	3,750
March 12 Q	7,992	14.5	3,731

Approximately 13,700 tonnes remains as a Bed Blend Stockpile on the ROM pad at the Raleigh Mine and will be hauled in early July.

Raleigh Underground Mine Development


At the end of the quarter, the bottom of the Raleigh Decline is at 5618 m RL, 727 m from the surface.

Development progressed on the 5631 and 5614 levels.


RALEIGH UNDERGROUND DEVELOPMENT					
Month	Capital		Operating		
	Decline (m)	Secondary (m)	Waste (m)	Ore (m)	Paste Fill (m)
April	0.0	0.0	12.0	77.7	40.0
May	0.0	0.0	68.1	9.2	48.0
June	0.0	0.0	41.3	27.9	35.0
June 12 Q	0.0	0.0	121.4	114.8	123.0
March 12 Q	0.0	0.0	37.6	257.1	136.0

The diagrams below show the status of the mine at the end of each month of the quarter.


April 12 Green indicates new development at Raleigh

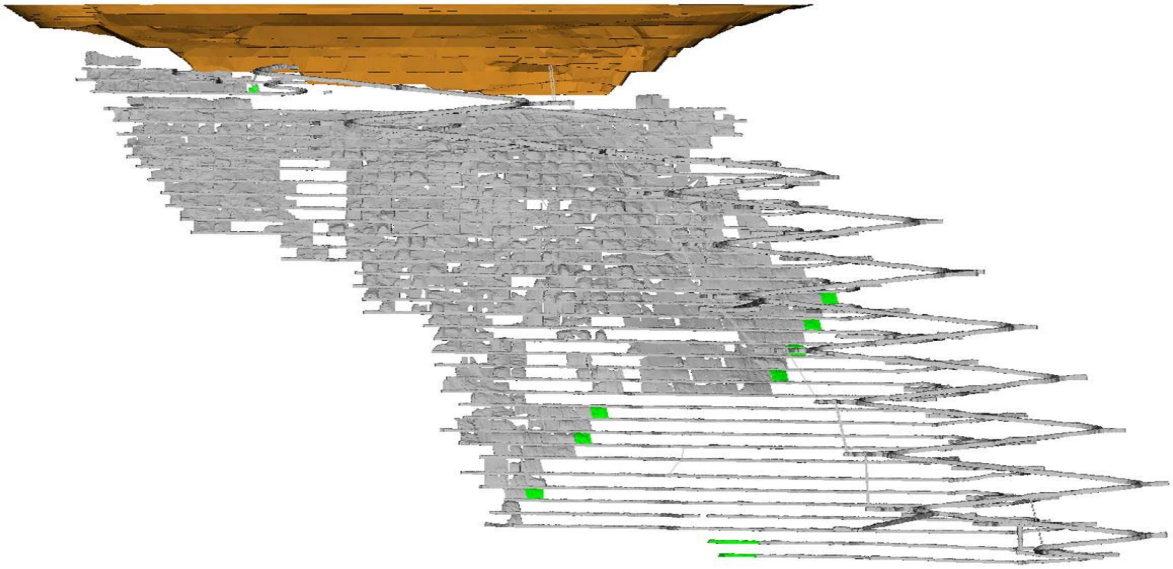

May 12 Green indicates new development at Raleigh

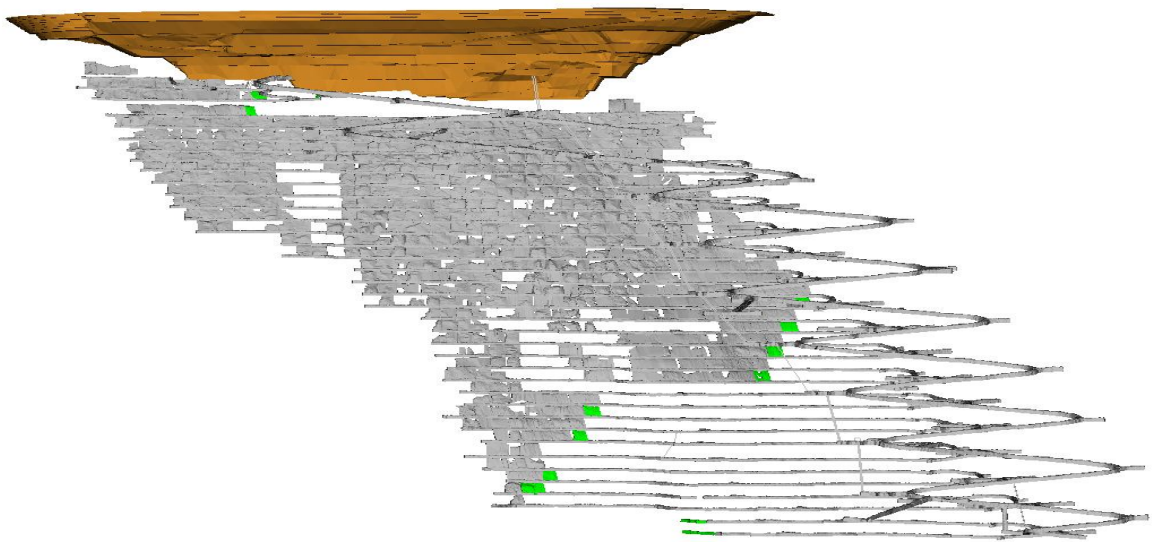

June 12 Green indicates new development at Raleigh

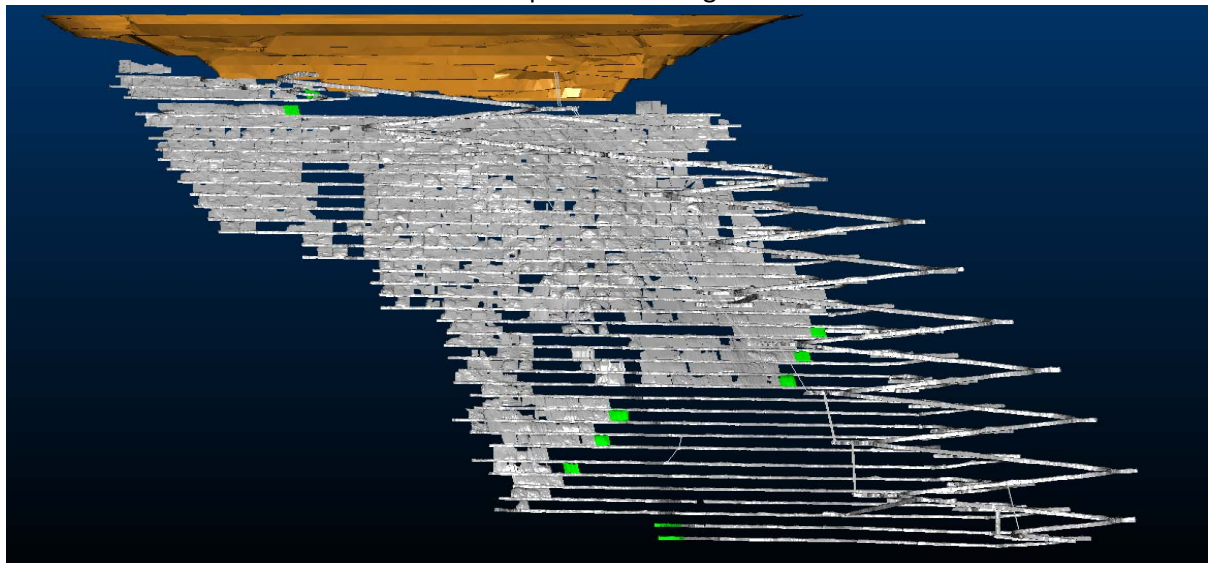

Mine operating costs incurred during the June 2012 Quarter were \$213 per tonne mined or \$384 per ounce mined compared with the March 2012 Quarter costs of \$200 and \$429 respectively.

Rubicon Underground Mine Production

During the quarter, development of the Rubicon ore body progressed on the 6135 and 6115 levels and the Hornet ore body on the 6165, 6145 and 6125 levels. Stope production from the Rubicon 6225 and 6195 levels continued during the quarter.

Contained gold in stope development mined during the quarter, estimated by grade control face chip sampling, is tabulated below:

RUBICON UNDERGROUND GRADE CONTROL ESTIMATES			
Month	Tonnes	Grade	Ounces
	t	g/t	troy oz
April	13,220	7.18	3,051
May	16,291	7.48	3,915
June	17,332	12.22	6,812
June 12 Q	46,843	9.1	13,778
March 12 Q	9,854	10.2	3,250

Rand's Entitlements (12.25%)

June 12 Q	5,738	9.1	1,688
March 12 Q	1,207	10.2	398

Approximately 2,000 tonnes remains as a Bed Blend Stockpile on the ROM pad at the Rubicon Mine and will be hauled in early July.

Rubicon Underground Mine Development

At the end of the quarter, the bottom of the Rubicon Decline is at 6067 m RL, 276 m from the surface, the bottom of the Hornet Decline is at 6076 m RL, 267 m from the surface and the top of the Hornet Incline is at 6183 m RL, 160 m from the surface.


RUBICON UNDERGROUND DEVELOPMENT					
Month	Capital		Operating		
	Decline (m)	Secondary (m)	Waste (m)	Ore (m)	Paste Fill (m)
April	168.9	176.2	31.6	177.8	10.0
May	198.3	115.0	32.6	236.9	5.0
June	182.5	161.0	24.0	248.7	0.0
June 12 Q	549.7	452.2	88.2	663.4	15.0
March 12 Q	512.6	871.2	73.2	120.7	0.0

The diagrams below show the status of the mine at the end of each month of the quarter.


April 12 Green indicates new development at Rubicon



May 12 Green indicates new development at Rubicon

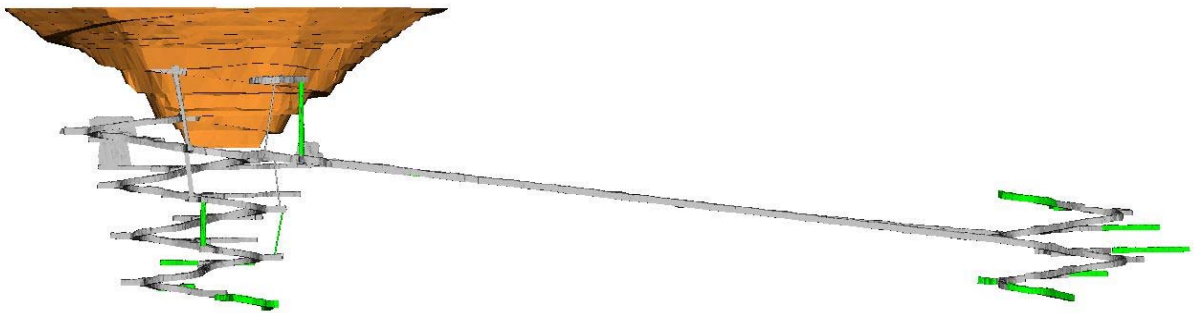

June 12 Green indicates new development at Rubicon

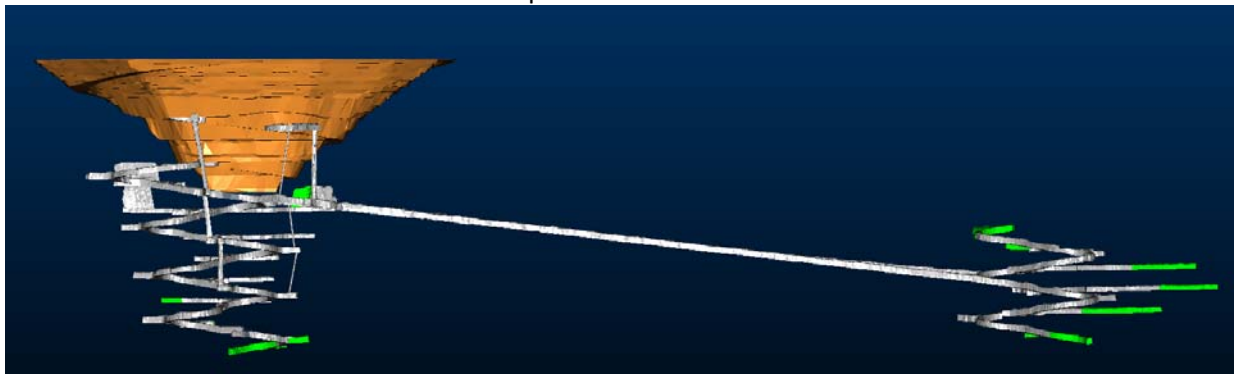

Toll Processing

During the quarter, 31,053 tonnes (wet) of Raleigh ore and 23,469 tonnes (wet) of Rubicon ore were hauled to the Greenfields Plant. The twenty second toll treatment campaign at the Greenfields Plant, which started on May 8, 2012, finished on May 31, 2012. During the quarter, 39,127 tonnes of EKJV ore were processed. At the end of the quarter, approximately 22,100 tonnes (wet) of Raleigh ore and 19,600 (wet) tonnes of Rubicon ore remain on the ROM pad at the Greenfields Plant.

Bullion accredited to RAND and TRIBUNE			
Quarter	Gold (oz)	Silver (oz)	Rand's share gold
June 12	13,419.595	4,926.422	3,354.897
March 12	17,311.273	6,030.152	4,327.816

EKJV Exploration

The 2102 drilling programme has commenced. Results will be announced when assays become available.

OTHER EXPLORATION

Wongan Hills (Rand's Interest 100%)

A drilling programme to test previously reported anomalies has been planned and will start when a drill rig is available.

Seven Mile Hill Joint Venture (Rand's Interest 50%)

Discussions to farm out the Seven Mile Hill tenements are continuing.

Tapeta Iron Ore Project, Liberia, West Africa

Construction of the camp on the lease continues. Work on the access road continues.
